Kansas Department of Agriculture

Water Rights Information System Mobile Application Development

ID	Task Name	Duration	Start	Finish
1	**Project Kickoff/Setup**	**108 days**	**Mon 3/17/14**	**Fri 8/15/14**
2	Project Setup	10 days	Mon 3/17/14	Fri 3/28/14
3	Kickoff Meeting	1 day	Thu 3/20/14	Thu 3/20/14
4	Kickoff Meeting Minutes and Project Plan	104 days	Thu 3/20/14	Thu 8/14/14
5	Detailed Project Plan Submittal	1 day	Fri 8/15/14	Fri 8/15/14
6	**Requirements Gathering**	**50 days**	**Tue 9/2/14**	**Tue 11/11/14**
7	Onsite Requirements Interviews	4 days	Tue 9/2/14	Fri 9/5/14
8	Requirements Spec Development	25 days	Mon 9/8/14	Fri 10/10/14
9	Draft Requirements Spec Submittal	1 day	Tue 10/21/14	Tue 10/21/14
10	Requirements Spec KDA Review	10 days	Wed 10/22/14	Tue 11/4/14
11	Requirements Spec Finalization	5 days	Wed 11/5/14	Tue 11/11/14
12	Requirements Spec Submittal	1 day	Tue 11/11/14	Tue 11/11/14
13	**Application Design**	**43 days**	**Mon 9/29/14**	**Wed 11/26/14**
14	Design Spec Development	35 days	Mon 9/29/14	Fri 11/14/14
15	Draft Design Spec Submittal	1 day	Fri 11/14/14	Fri 11/14/14
16	Design Spec KDA Review	5 days	Mon 11/17/14	Fri 11/21/14
17	Design Spec Finalization	4 days	Sat 11/22/14	Wed 11/26/14
18	Design Spec Submittal	1 day	Wed 11/26/14	Wed 11/26/14
19	**Application Development**	**20 days**	**Mon 12/1/14**	**Mon 12/29/14**
20	Application Coding	20 days	Mon 12/1/14	Mon 12/29/14
21	**Application Testing**	**20 days**	**Fri 12/26/14**	**Fri 1/23/15**
22	BMcD Application Testing	20 days	Fri 12/26/14	Fri 1/23/15
23	**Application Deployment**	**1 day**	**Mon 1/26/15**	**Mon 1/26/15**
24	KDA Onsite Application Deployment	1 day	Mon 1/26/15	Mon 1/26/15
25	**Documentation and Training**	**11 days**	**Sat 1/10/15**	**Mon 1/26/15**
26	User's Manual Development	9 days	Sat 1/10/15	Wed 1/21/15
27	User Acceptance Testing Team Training	1 day	Mon 1/26/15	Mon 1/26/15
28	**User Acceptance Testing**	**16 days**	**Tue 1/27/15**	**Tue 2/17/15**
29	KDA User Acceptance Testing	10 days	Tue 1/27/15	Mon 2/9/15
30	Application Adjustments	5 days	Tue 2/10/15	Mon 2/16/15
31	Final Application Deployment	1 day	Tue 2/17/15	Tue 2/17/15
32	Post Implementation Support	24 days	Wed 2/18/15	Mon 3/23/15
33	Annual Maintenance	257 days	Wed 2/18/15	Wed 2/17/16
34	Annual Custom Code Support	257 days	Wed 2/18/15	Wed 2/17/16

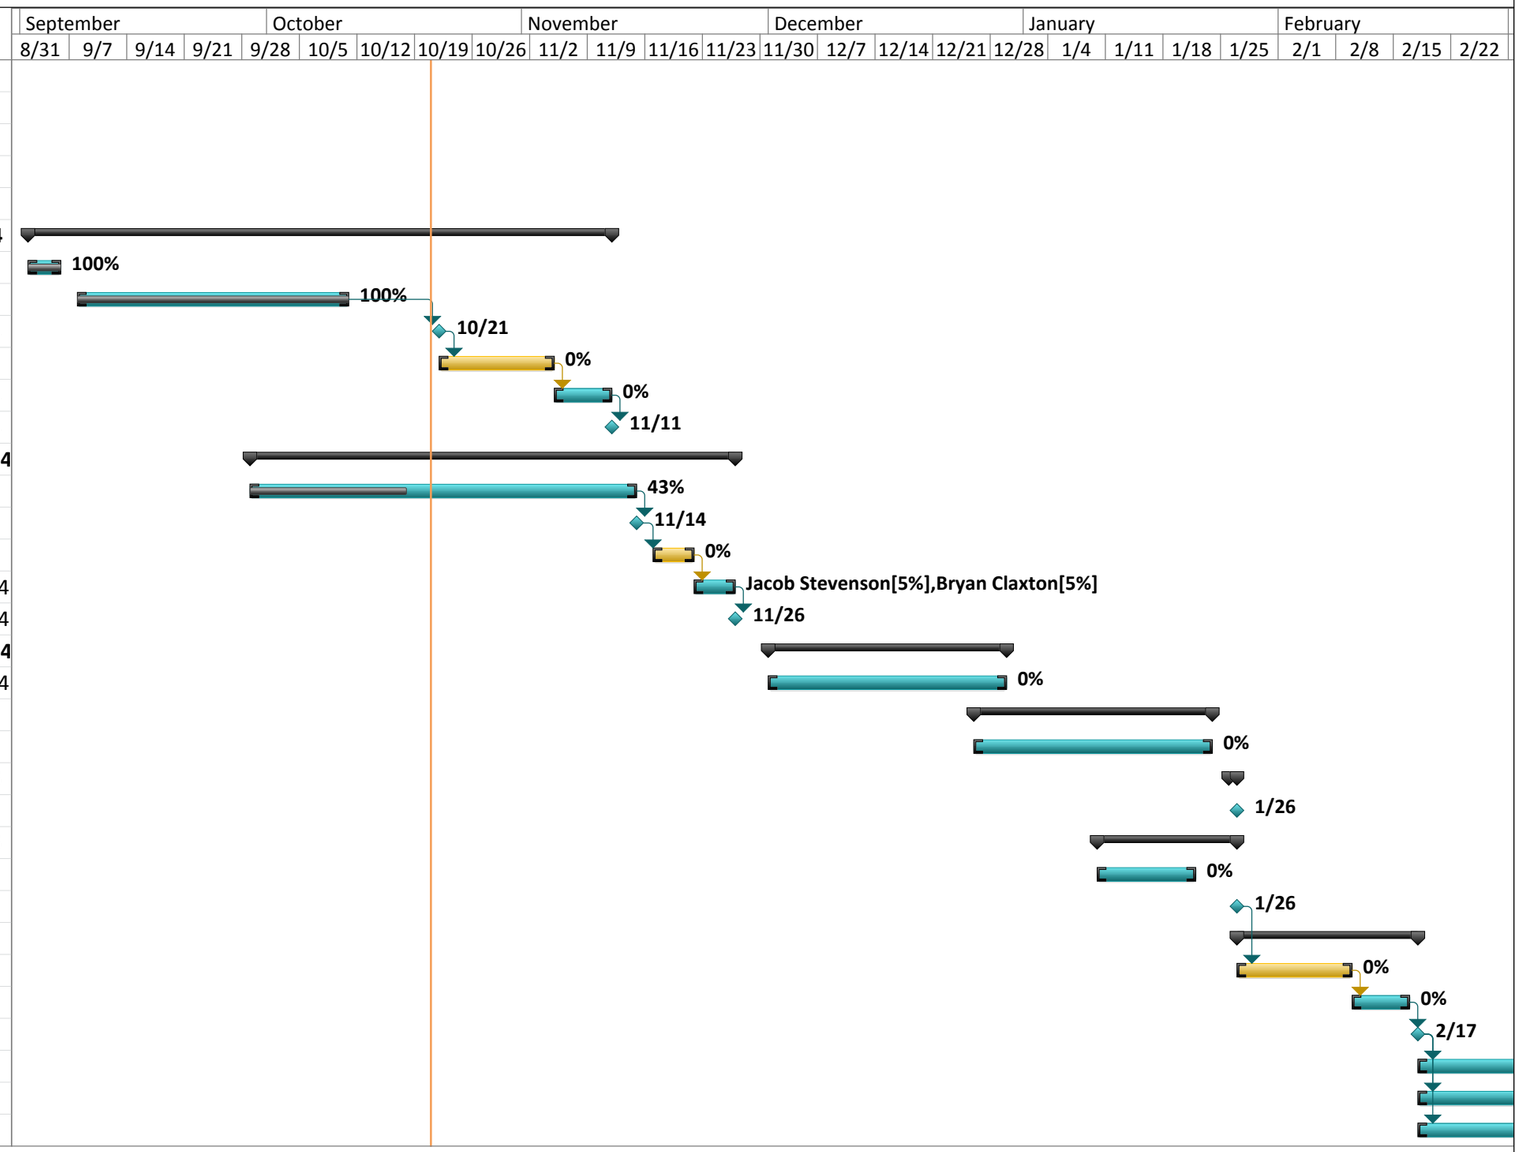

Project: 78288-WRISMobileApplic
Date: Tue 10/21/14

Task	Project Summary	Inactive Milestone	Manual Summary Rollup	Deadline	
Split	External Tasks	Inactive Summary	Manual Summary	Progress	
Milestone	External Milestone	Manual Task	Start-only		
Summary	Inactive Task	Duration-only	Finish-only		
